

Business Requirements Document (BRD)

Project: CraftCart – Online Handicrafts Marketplace

Version: 1.0 (Final Draft)

Document Owner: Business Analyst – Yash

Last Updated: 08-Sep-2025

Version History

Version	Date	Author	Reason for Change
0.1	Draft	Yash	First draft (template + sample content)
1.0	08-Sep-2025	Yash	Finalized draft with learnings merged

Table of Contents

1. Executive Summary
2. Project Details
3. Business Objectives & Success Metrics
4. Scope
5. Stakeholders & RACI
6. Business Requirements (High-Level)
7. Non-Functional Requirements
8. Business Process Overview
9. Assumptions & Constraints
10. Dependencies
11. Risks & Mitigations
12. Prioritization & Release Strategy
13. Acceptance & Success Criteria
14. Change Control & Traceability
15. Reporting & Analytics
16. Compliance & Data Governance
17. Budget (High-Level)
18. Glossary
19. Attachments & Links
20. Final Sign-off

1. Executive Summary

CraftCart will launch a curated marketplace connecting Indian artisans and micro-sellers with buyers seeking authentic handicrafts. Today, sellers struggle with digital onboarding, trust, and last-mile logistics; buyers lack discovery and quality assurance. CraftCart aims to provide a secure, scalable, and user-friendly platform comparable to category leaders while preserving artisanal storytelling. Phase-1 targets an MVP within 12 weeks, followed by growth and optimization releases. Success will be measured by GMV, active users/vendors, order success rate, NPS, and compliance adherence.

2. Project Details

Field	Value
Project Type	New Build
Start / End Dates	01-Oct-2025 – 31-Mar-2026
Sponsor	TBD
Primary Driver	Revenue growth via marketplace expansion
Secondary Driver	Customer experience & compliance
Division	Digital Commerce
Product Manager	TBD
BA	Yash

3. Business Objectives & Success Metrics

1. **Acquire users:** Reach **10,000 MAU** within **6 months** of launch.
2. **Onboard sellers:** **1,000 verified vendors** with KYC passed in 6 months.
3. **Conversion:** Product page → purchase conversion $\geq$ **2.5%**.
4. **Reliability:** Checkout success $\geq$ **99.5%**; payment success $\geq$ **98.5%**.
5. **CSAT/NPS:** Post-purchase NPS $\geq$ **45** by month-6.
6. **Compliance:** 0 critical audit findings for data privacy & payments.

4. Scope

In-Scope (MVP): - E-commerce web application (mobile-responsive).

- Integration with **payment gateways** (UPI, cards via tokenization).
- User account management (login, registration, profile).
- Product catalog management (categories, listings, media, pricing).
- Shopping cart and **secure checkout**.
- Order processing, tracking, and notifications.
- Integrations with third-party systems (KYC, logistics; Phase-2: inventory/CRM/ERP).

Out-of-Scope (MVP): - Marketing campaign execution.

- Backend integration for **non-commerce** internal systems (HR/Finance).
- Physical infrastructure setup (warehousing/logistics ops).

Release Plan: MVP (T0), Growth (T0+8w), Optimization (T0+16w).

5. Stakeholders & RACI

Stakeholder Group	Role / Interest	Responsibilities
Business Sponsor	P&L owner	Approves scope & budget, removes roadblocks
Product	Product strategy	Prioritization, roadmap, acceptance
BA	Requirements & alignment	Elicitation, documentation, RTM, change control
Engineering	Build & integrate	Solution feasibility, estimates, delivery
Design/UX	Experience	IA, flows, accessibility
QA	Quality	Test strategy, UAT coordination
Compliance/Legal	Privacy/Regulatory	KYC/AML, data retention, T&C
Payments	Gateway/UPI	Payment options, reconciliation
Logistics	Fulfilment	Partner SLAs, tracking
Vendors (Sellers)	Supply	Catalog quality, KYC documents
Customers (Buyers)	Demand	Feedback, beta/UAT

6. Business Requirements (High-Level)

Marketplace & Discovery

- **BR-01 (Must):** Browse categories, filter/sort, view product details + artisan story.
- **BR-02 (Must):** Search with typo tolerance and facets.
- **BR-13 (Could):** Recommendation engine based on behavior & history.

Vendor Onboarding & KYC

- **BR-03 (Must):** Sellers register with OTP + KYC (PAN/Aadhaar), bank details; status lifecycle.
- **BR-15 (Must):** Seller dashboard for listing, inventory, orders, payouts, metrics.

Checkout & Payments

- **BR-04 (Must):** Guest & logged-in checkout; addresses; shipping options.
- **BR-05 (Must):** UPI (intent & collect), cards (tokenized), COD (Phase-2).

Orders & Fulfilment

- **BR-06 (Must):** Order placement, cancellations, returns/refunds, **proactive notifications**.

Support & Engagement

- **BR-07 (Should):** Ratings/reviews with moderation.
- **BR-08 (Should):** CMS for artisan profiles, blogs, pages.
- **BR-14 (Should):** Wishlist / Save for later.

Analytics

- **BR-09 (Must):** Dashboard for KPIs (GMV, AOV, CAC, funnel).

Compliance & Security

- **BR-10 (Must):** PDPB/GDPR controls, consent, deletion, audit logs.

Performance & Scalability

- **BR-11 (Must):** Handle $\langle \text{peak} \rangle$ of X TPS checkout with $\leq$ p95 2s load.


Internationalization (Future)

- **BR-12 (Could):** Multilingual content & prices.
-

7. Non-Functional Requirements

Category	Target
Availability	99.9% monthly
Performance	p95 page load $\leq$ 2s (home), $\leq$ 3s (PDP), checkout API $\leq$ 800ms
Security & Privacy	RBAC, encryption, consent, data deletion
Compliance	India PDPB, PCI-DSS via PSP
Accessibility	WCAG 2.1 AA
Localization	EN (Phase-1), HI/MR (Phase-2)
Observability	Central logs, SLO dashboards, alerts

8. Business Process Overview

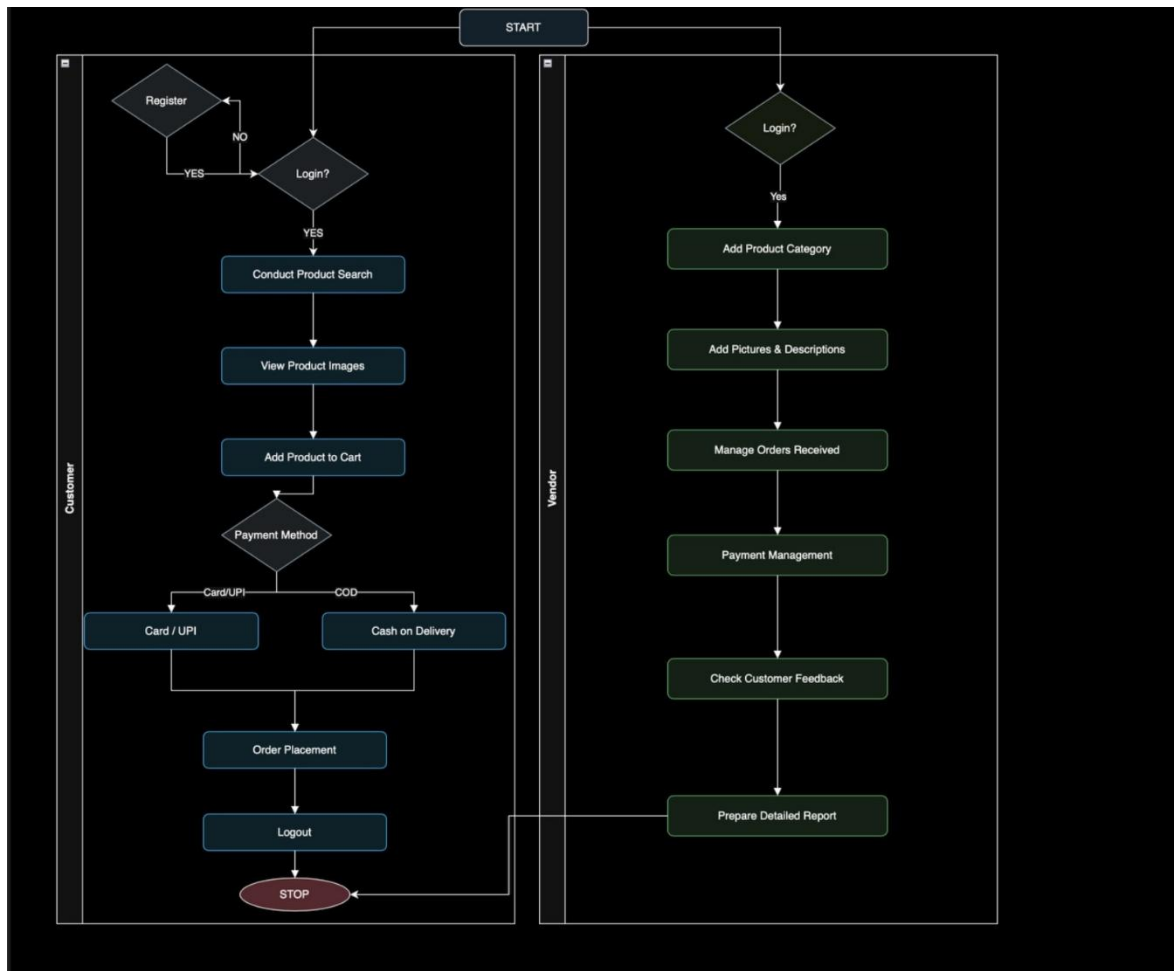

9. Assumptions & Constraints

- Website available 24×7 outside maintenance.
 - Existing user base continues post enhancements.
 - Third-party services (gateways, logistics, recommendations) stable.
 - Payments handled via PSP; no PAN storage.
 - Logistics via partners; COD limited.
 - Budget capped at ₹X; team capacity N devs).
 - Legal entity & GST in place before go-live.
-

10. Dependencies

- Payment PSP onboarding.
- KYC verification service.
- Logistics partner APIs.
- Artisan content & imagery.

11. Risks & Mitigations

ID	Risk	Likelihood	Impact	Exposure	Owner	Response
R-01	UPI timeouts	M	H	M-H	Payments	Multi-PSP, retries
R-02	KYC delays	M	M	M	Ops	Auto-validation, SLAs
R-03	Privacy non-compliance	L	H	M	Compliance	DPIA, logs
R-04	Festive load spike	M	H	H	Eng	Load test, scaling
R-05	Technical complexities	M	H	H	Eng	PoCs, phased rollout
R-06	Budget overruns	H	M	H	PM	Cost reviews, guardrails
R-07	Vendor integration delays	M	H	H	Partner Mgr	Backup vendors
R-08	Security risks	H	H	H	Sec Lead	Pentests, WAF
R-09	Low adoption	M	M	M	Marketing	Incentives, SEO

12. Prioritization & Release Strategy

Method: WSJF + MoSCoW.

MVP: BR-01, 03–07, 09–11, 15.

Phase-2: Reviews, loyalty, multilingual, recommendations.

Priority View | Value | Rating | Description | |---|---|---| | 1 | Critical | Order Management (cart, mgmt, place order) | | 2 | High | Payment Integration (navigate, select, pay) | | 3 | Medium | User Management (reg, login, linking) | | 4 | Low | Performance & Security testing (NFR visibility) |

13. Acceptance & Success Criteria

- KPIs in Section 3 achieved.
- UAT sign-off; no Sev-1 defects.
- Compliance sign-off (privacy & payments).

- Operational readiness (support runbooks, on-call, dashboards).
-

14. Change Control & Traceability

- Changes post sign-off require CRs.
 - RTM: BR-ID → Epics/Stories (Jira) → Test Cases → Release.
-

15. Reporting & Analytics

- Funnel (Sessions → PDP → Cart → Checkout → Paid).
 - GMV, AOV, CAC proxy, repeat rate, churn.
 - Seller: time-to-live, rejections, OTD%.
 - Ops SLOs: payment success, refund TAT, support TAT.
-

16. Compliance & Data Governance

- Data inventory, consent UX, DSR handling.
 - Retention, backups, auditability.
 - Third-party DPIAs (PSP, KYC, logistics).
-

17. Budget (High-Level)

Buckets: product/design, engineering, infra, PSP/KYC vendors, marketing, support.
Benefits: GMV uplift, artisan reach, CX differentiation.

18. Glossary

MAU, GMV, AOV, CAC, NPS, PDP, KYC, UPI, PSP, DPIA, DSR, SLO, RTM, MVP.

19. Final Sign-off

By signing below, both parties agree that this BRD reflects the agreed scope, timelines, budget, and deliverables. Any changes post-sign-off will follow the **Change Control** process outlined in Section 14.

Client – CraftCart Service Provider – Shellcode IT Services

Authorized Signatory

Title

Signature

Date
